


Carey Avenue Improvements

Pecos Road to Nellis Boulevard · Bid No. 607861-25

WEEK OF AUGUST 23 – 29, 2026

LANE CLOSURES & RESTRICTIONS

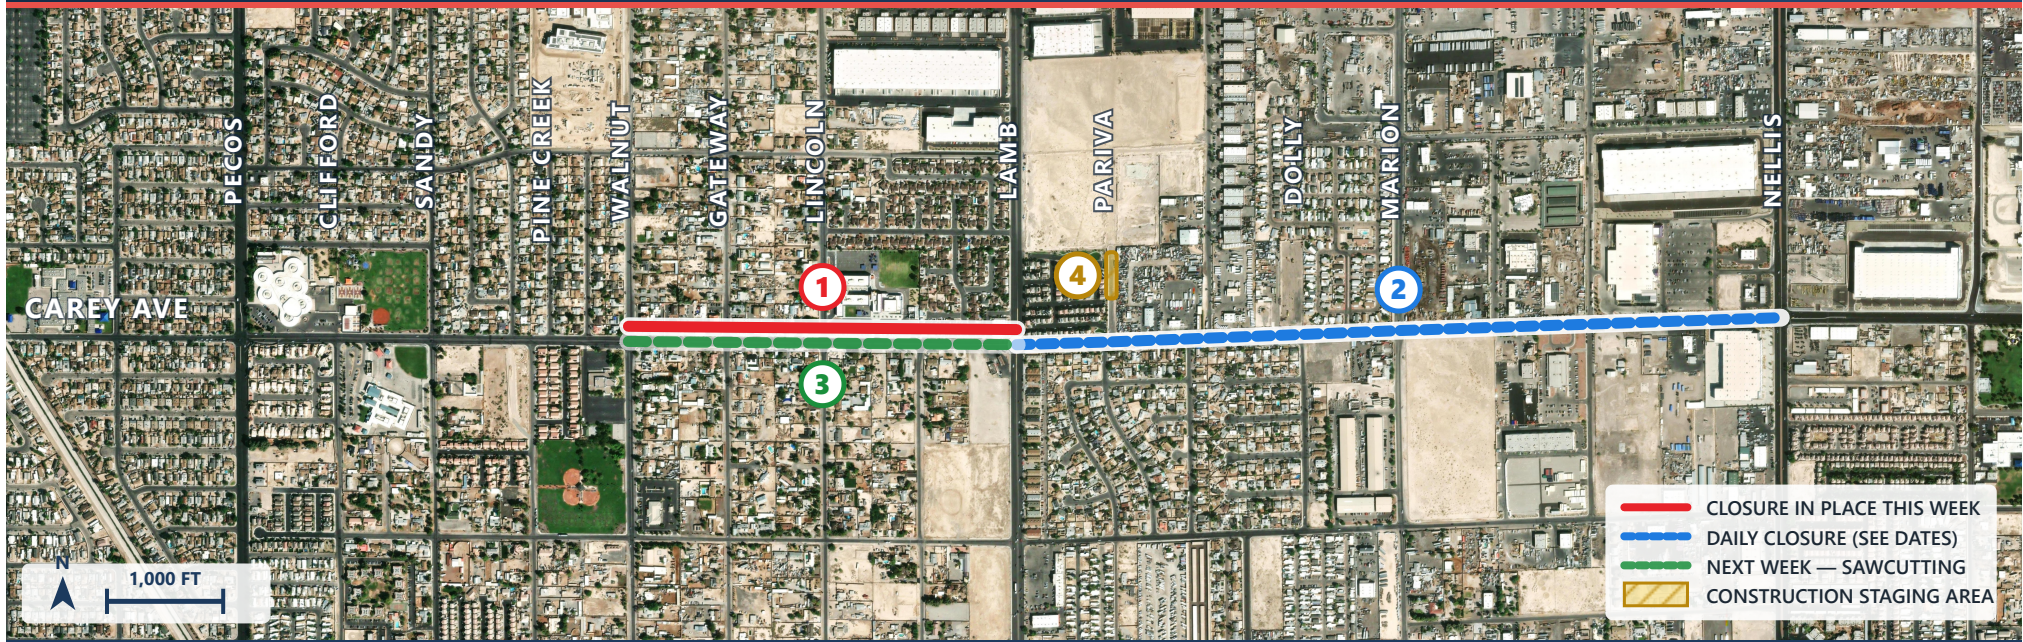

WORK DAYS & TIMES

Crew working hours: 7:00 AM – 3:30 PM,
Mon–Fri

ABOUT THIS WORK

Crews are installing underground fiber-optic (ITS) conduit and pull boxes along the north side of Carey Avenue, working east from Walnut Rd toward Lamb Blvd over the next two weeks. Crews are also sawcutting concrete — spandrels and valley gutter — on both sides of the road, this week between Lamb Blvd and Nellis Blvd, moving to the Walnut Rd to Lamb Blvd segment next week. This sawcutting does not involve the asphalt roadway.

The ITS lane closure remains in place through the week of August 30 – September 5. Daily sawcutting closures shift west to the Walnut Rd – Lamb Blvd segment that week.

THIS WEEK'S CLOSURES & RESTRICTIONS

1 Carey Avenue — Walnut Rd to Lamb Blvd (Westbound)

Right lane closure, westbound (north lane), from Walnut Rd to Lamb Blvd for ITS conduit trenching and pull box installation. This closure remains in place this week and next week. Westbound traffic maintained in the remaining lane; all driveways remain accessible.

3 Carey Avenue — Walnut Rd to Lamb Blvd (Eastbound & Westbound)

NEXT WEEK

Beginning next week (August 30 – September 5), daily right lane closures, eastbound and westbound, between Walnut Rd and Lamb Blvd for sawcutting of concrete spandrels, valley gutter, and other concrete removals — no asphalt roadway work. Closure locations and direction vary daily, set up only where sawcutting is anticipated, after school bell hours. Traffic maintained in the remaining lane; all driveways remain accessible.

2 Carey Avenue — Lamb Blvd to Nellis Blvd (Eastbound & Westbound)

DAILY

Daily right lane closures, eastbound and westbound, between Lamb Blvd and Nellis Blvd for sawcutting of concrete spandrels, valley gutter, and other concrete removals — no asphalt roadway work. These daily closures are in place this week only; sawcutting moves west to the Walnut Rd – Lamb Blvd segment next week. Closure locations and direction vary daily, set up only where sawcutting is anticipated, after school bell hours. Traffic maintained in the remaining lane; all driveways remain accessible.

4 Pariva Street — North End

Construction staging area on the north end of Pariva St, in place for the duration of the project. All driveways on Pariva St remain accessible from Carey Ave.
