
CLARK COUNTY PUBLIC WORKS · PROJECT TRAFFIC ADVISORY

Carey Avenue Improvements

Pecos Road to Nellis Boulevard · Bid No. 607861-25

WEEK OF OCTOBER 11 – 17, 2026

LANE CLOSURES & RESTRICTIONS

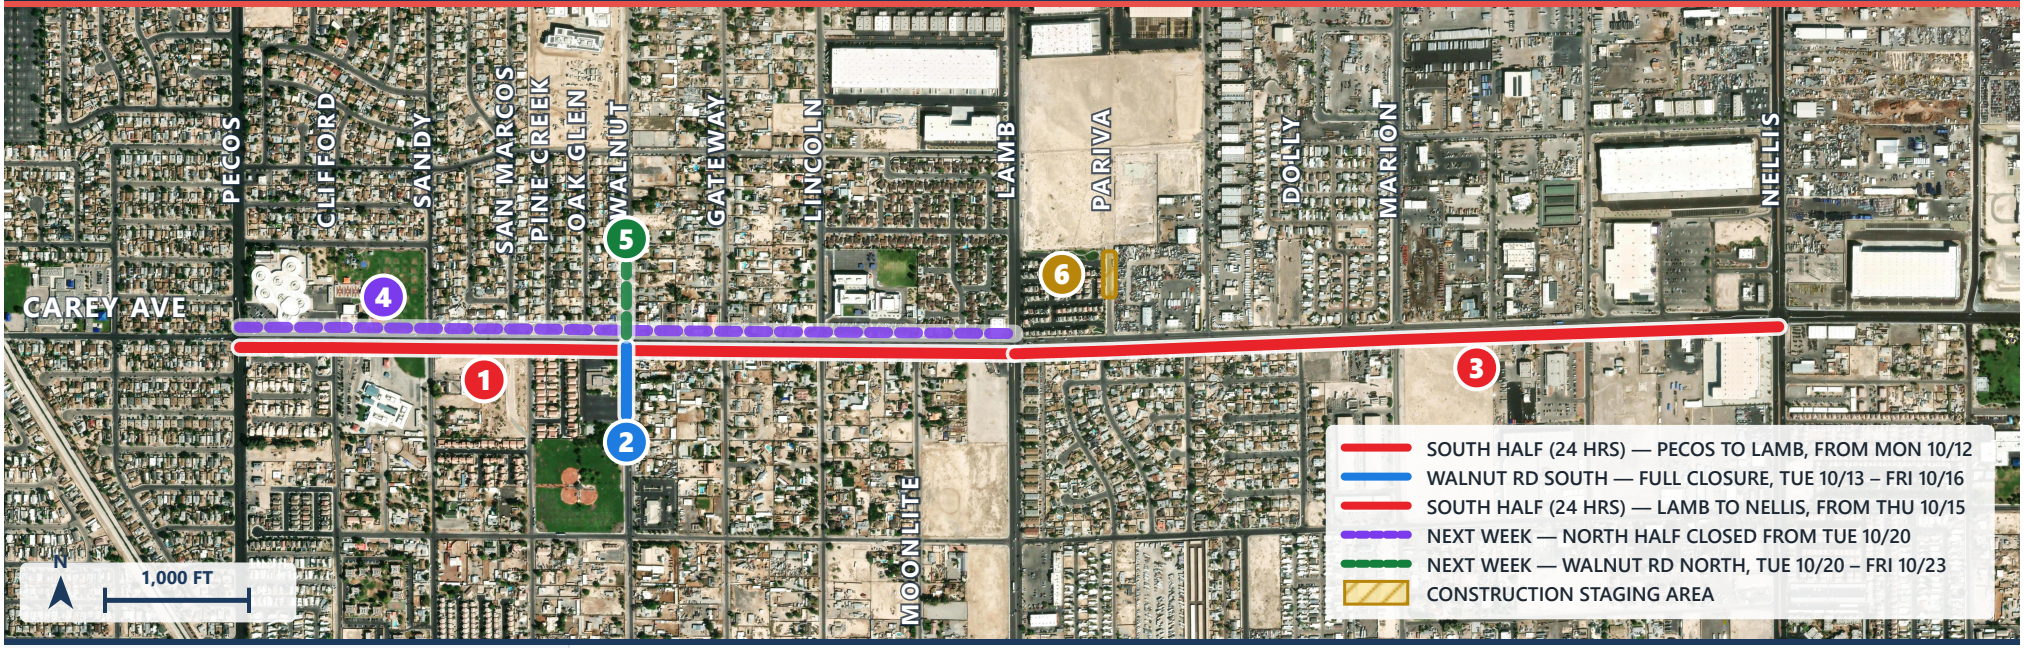

WORK DAYS & TIMES

Crew working hours: 7:00 AM – 3:30 PM, Monday–Friday

ABOUT THIS WORK

Asphalt paving begins this week. Starting Monday, October 12, the south half of Carey Ave is closed around the clock from Pecos Rd to Lamb Blvd while crews mill and repave it; the south half from Lamb Blvd to Nellis Blvd follows Thursday, October 15. Walnut Rd south of Carey is fully closed Tuesday through Friday, October 13–16, for full-depth reconstruction. One lane in each direction plus the left-turn lanes at the signals stay open on Carey at all times; flaggers assist with driveways. Next week, work moves to the north half.

> Dates assume clear weather. If rain delays the work, each date shifts by the same number of days.

CLOSURES & RESTRICTIONS — OCTOBER 11 – 17

1 Carey Avenue — Pecos Rd to Lamb Blvd (South Half)

FROM MON 10/12

South half of Carey Ave closed around the clock, Pecos Rd to Lamb Blvd, for milling (Monday–Wednesday) and paving (Thursday, October 15 and Monday, October 19). Eastbound and westbound traffic share the north half, one lane in each direction, with left-turn lanes open at the signals. Flaggers help residents and businesses in and out of driveways. The closure is removed as paving is completed, expected Monday, October 19.

2 Walnut Road — South of Carey Ave (Full Closure)

TUE 10/13 – FRI 10/16

Walnut Rd is closed from Carey Ave to the south, Tuesday through Friday, October 13–16, for full-depth reconstruction (mill, subgrade, base, pave). No through traffic; residents reach their driveways with a flagger's help. Walnut Rd north of Carey stays open. Reopens Friday evening, October 16.

3 Carey Avenue — Lamb Blvd to Nellis Blvd (South Half)

FROM THU 10/15

South half of Carey Ave closed around the clock, Lamb Blvd to Nellis Blvd, beginning Thursday, October 15, for milling (Thursday–Monday) and paving (Tuesday–Thursday, October 20–22). Traffic shares the north half, one lane in each direction, with left-turn lanes open at the signals. Driveways remain accessible with flagger assistance. Expected removal Thursday, October 22.

4 Carey Avenue — Pecos Rd to Lamb Blvd (North Half)

NEXT WEEK

FROM TUE 10/20 Beginning Tuesday, October 20, the north half of Carey Ave, Pecos Rd to Lamb Blvd, is closed around the clock for milling and paving. Both directions of traffic run on the newly paved south half, one lane in each direction. Where the north-half and south-half work meet at Lamb Blvd (October 20–22), traffic crosses from one side to the other at the Lamb signal.

5 Walnut Road — North of Carey Ave (Full Closure)

NEXT WEEK

TUE 10/20 – FRI 10/23 Walnut Rd is closed from Carey Ave to the north, Tuesday through Friday, October 20–23, for full-depth reconstruction. No through traffic; residents reach their driveways with a flagger's help. Walnut Rd south of Carey (rebuilt the week before) stays open.

6 Pariva Street — North End

Construction staging area on the north end of Pariva St, in place for the duration of the project. All driveways on Pariva St remain accessible from Carey Ave.

Imagery: Esri, Maxar, Earthstar Geographics, and the GIS User Community
